

1. DESCRIPTION OF WORKS AND PHOTOGRAPHIC REPORT

Listed below are all the works carried out by **3RS GESTIÓN** for the Urban Solid Waste Collection Service, Street Cleaning and Maintenance of the Green Areas of the urban entity "Hacienda del Álamo Golf Resort", in **JUNE 2026**.

1.1. MUNICIPAL SOLID WASTE WORKS

Resolution regarding the **ACT OF VANDALISM** in which the seals and signage on the selective waste collection boxes in front of the Pueblo Español underground parking garage were removed. The EUC has been informed.



Before



After

At the request of the EUC and on the occasion of the Pueblo Español Party that were held from June 6 to 9, 4 additional 800L residual fraction containers were placed, in addition to a selective island made up of 3 containers of packaging + cardboard + glass.



Following the end of the Pueblo Español Party and at the request of the EUC, it was decided to leave the selective island of 3 containers (packaging + cardboard + glass) permanently in the rear parking lot and 2 additional 800L residual fraction containers (in C/ Mojácar and in the entrance parking lot).





1.2. STREET CLEANING WORKS

At the request of the EUC and on the occasion of the Pueblo Español Party held from June 6 to 9, a series of additional cleaning services were carried out consisting of:



PLANNING OF MSW COLLECTION AND STREET CLEANING WORK OF PUEBLO ESPAÑOL PARTY				
JUNE 2026	FRIDAY 5	SATURDAY 6	SUNDAY 7	MONDAY 8
BRIGADE 01	REGULAR MSW COLLECTION	EXTRAORDINARY COLLECTION OF MSW	EXTRAORDINARY COLLECTION OF MSW	REGULAR MSW COLLECTION
BRIGADE 02	CLEANING SQUARES & BINS		CLEANING OF SQUARES, BINS AND CLEANING OF TENT AREA (INT. & EXT.)	CLEANING OF SQUARES, BINS AND CLEANING OF TENT AREA (INT. & EXT.)








1.3. GARDENING WORKS

Trimming of hedges and ficus trees, clearing and cleaning of the Main Road, from Phase 1 roundabout to Black Gravel roundabout

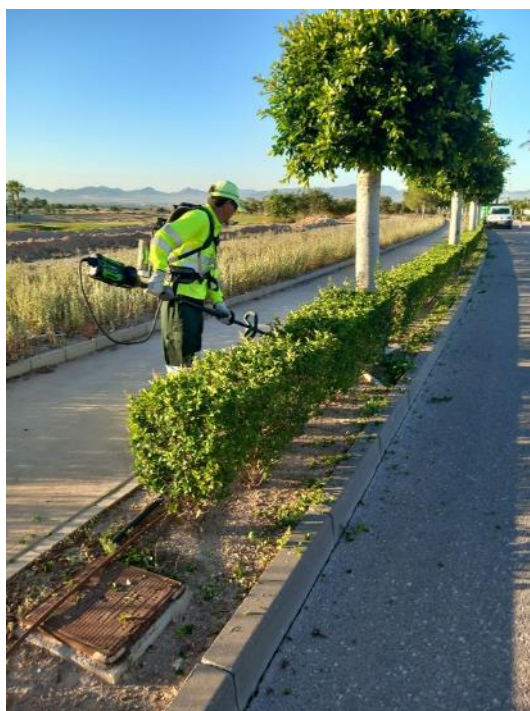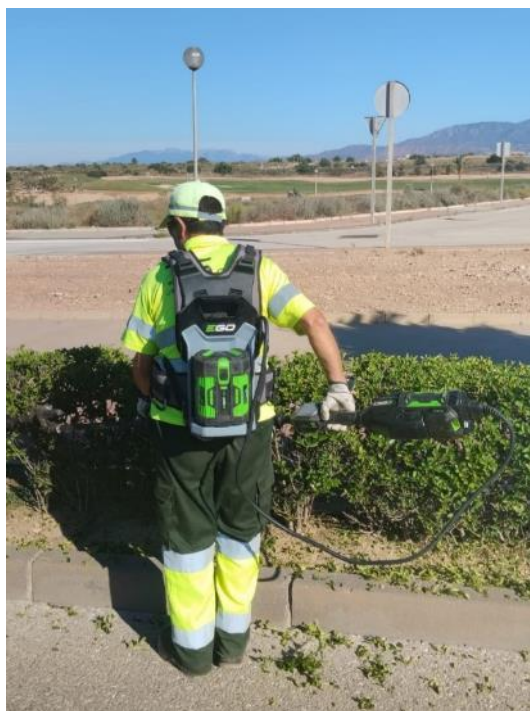

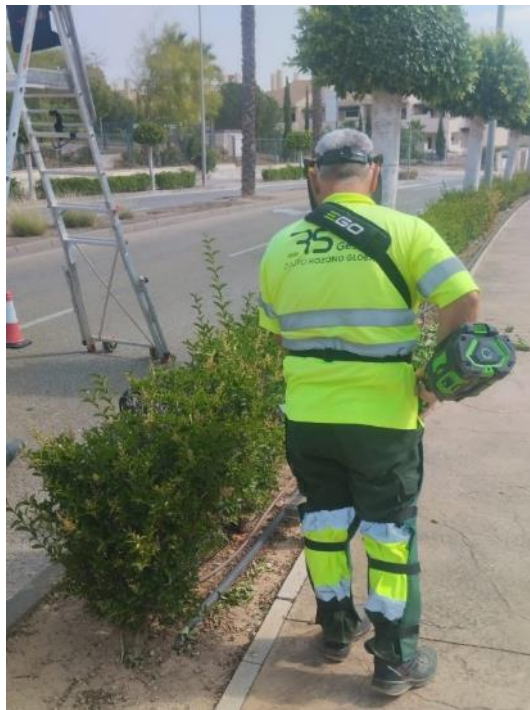




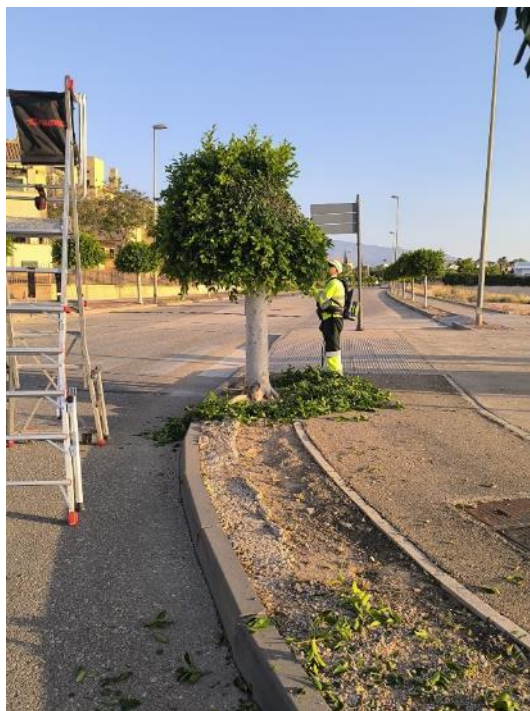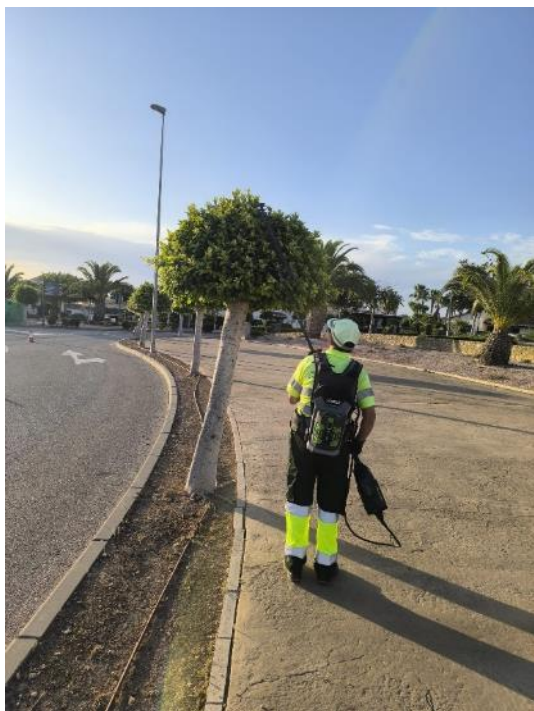

Trimming of hedges and ficus trees, clearing and cleaning of interior streets and sidewalks in Phases 2-3



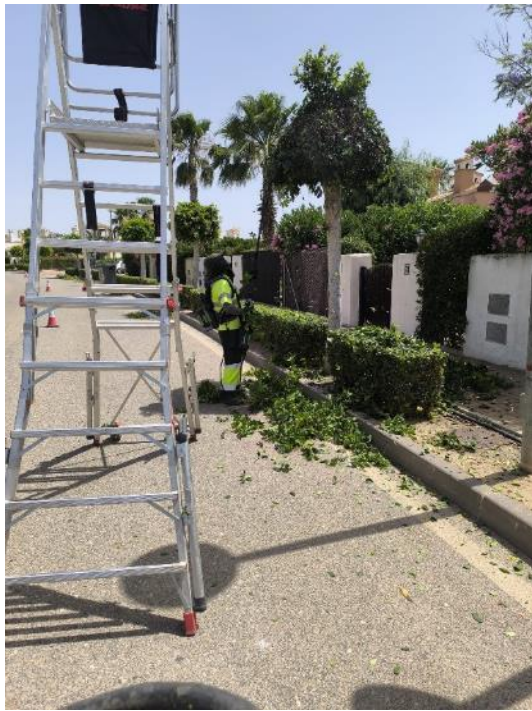



Trimming of hedges and ficus trees, clearing and cleaning on Paseo Alameda in Phase 7 Oasis





Trimming of hedges and ficus trees, clearing and cleaning of the road leading to Pueblo Español (C/ Calabardina)



Hedge trimming, clearing and cleaning of the park next to the MULTI-PURPOSE BUILDING



Mowing the driveway lawn, the square garden, the driveway roundabout, the Phase 6 roundabout, and the Phase 1 roundabout





New flower planting in the entrance roundabout. Removal of existing dried plants, addition of organic matter, tilling, and new spring planting of orange/yellow mixed-color Tagetes





Draining, pressure washing, filling and tuning of the ornamental fountain at the entrance






Phytosanitary treatments against weeds in Main Road, Park next to Security Booth, Long Park in Road B and Pine Grove opposite Hotel





Phytosanitary treatments against aphids in hedges and street ficus trees on Main Road

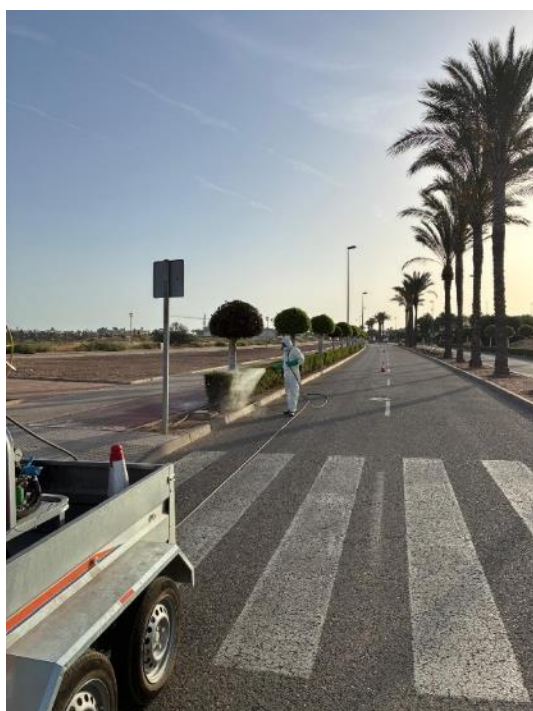



Mowing the driveway lawn, the square garden, the driveway roundabout, the Phase 6 roundabout, and the Phase 1 roundabout



Weekly and monthly monitoring of temperature, pH and chlorine levels in facilities susceptible to Legionella proliferation (ornamental fountain, sprinkler irrigation and tanks)



Review of the irrigation network, opening manholes and checking controllers, solenoid valves, and emission points, detecting and repairing each of the incidents detected at the following locations:



Entrance - Garden by Squares (replacement of 1 Rain Bird programmer by Solem 2E)



Entrance - Garden by Squares (refill 3 ml PE Ø32, 2 links)



Entrance - Garden by Squares (replacement of the rest of the garden with 7 new SOLEM programmers)



Entrance - Garden by Squares (replacement of the rest of the garden with 7 new SOLEM programmers)



Entrance - Garden by Squares (replacement of the rest of the garden with 7 new SOLEM programmers)



Entrance - Garden by Squares (replacement of the rest of the garden with 7 new SOLEM programmers)



Phase 6 - C/ Guinea garden (repair leak 0.5 ml PE Ø16, 2 links)



Phase 6 - Olivos Garden B (repair ring 2 ml PE Ø16, 2 links, 2 drippers)



Phase 6 - Olivos Garden B (repair ring 2 ml PE Ø16, 2 links, 2 drippers)



Main Road - C/ Vistas Green garden (refill 70 ml PE Ø16, 6 links)



Main Road - C/ Vistas Green garden (refill 70 ml PE Ø16, 6 links)



Main Road - Sports fields (2 ml repair PE Ø32, 2 links)



Main Left Road - Maintenance (replacement of broken Solem programmer with new SOLEM)



Main Road Right - Maintenance (replacement of Rain Bird programmer with a new SOLEM)



Phase 6 - Olivos A (repair of old cracked pipe 23 ml PE Ø16, 6 links)



Phase 6 - Olivos A (repair of 10 ml PE Ø32 pipe, 4 links)
